






OWNER:  شرکت سست و سویی توهمه ایران (سهامی خاص)	BUSHEHR PETROCHEMICAL COMPANY MEG PLANT						EPC CONTRACTOR:  Chagalesh-Enerchimi-Steam Joint Venture BUPC-MEG PLANT PROJECT		
	TIME SCHEDULE								
MC :  شرکت سست و سویی توهمه ایران (سهامی خاص)	Project	Area	Phase	Unit	Dis.	Doc.	Seq.	Contract No : 52-98/445	
Owner Document Number: 17811-73	BU	20	VD	303	PC	SCH	0003	Rev.:	Page
								03	1 of 4

TIME SCHEDULE

Rev.	Date	Purpose of Issue	Prepared	Checked	Approved	AC Code
03	27/11/2024	Issue For Review	JR	KP	PW	
02	05/10/2021	Issue For Review	JR	KP	PW	
01	14/09/2021	Issue For Review	JR	KP	PW	
00	21/07/2021	Issue For Review	JR	KP	PW	
					Class: 2	Phase: P



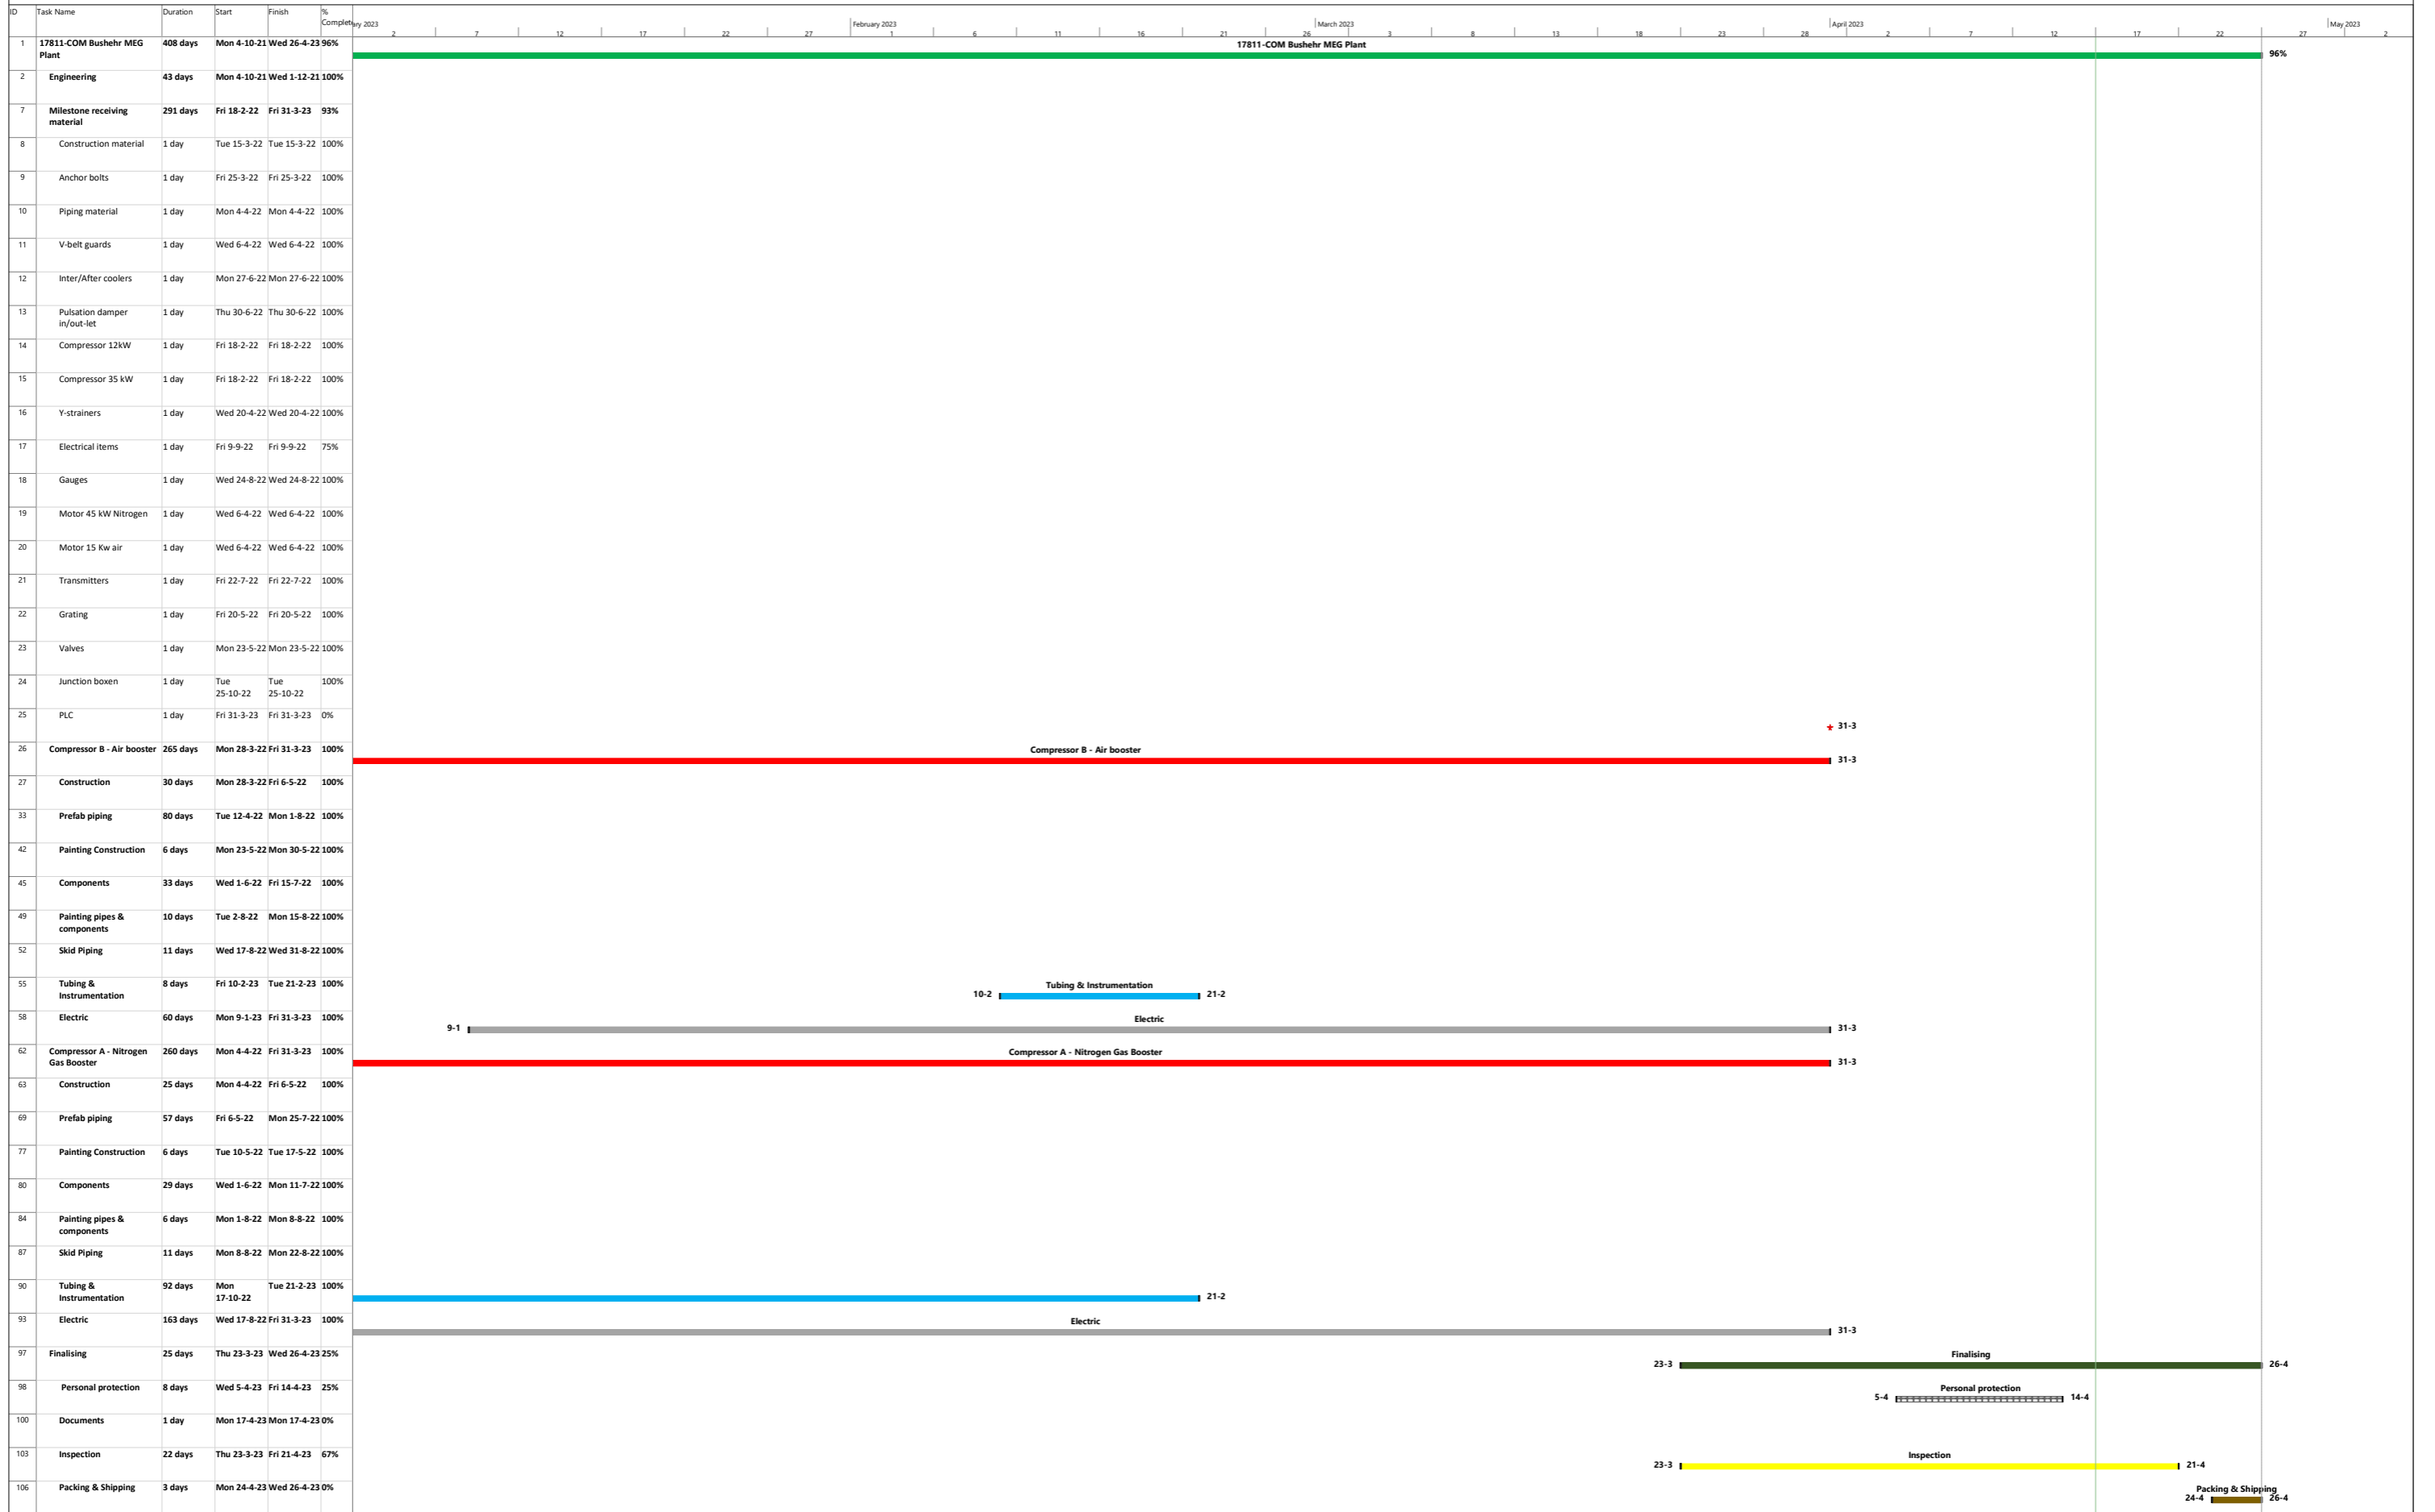

ID	Task Name	Duration	Start	Finish	% Complete
1	17811-COM Bushehr MEG Plant	408 days	Mon 4-10-21	Wed 26-4-23	96%
2	Engineering	43 days	Mon 4-10-21	Wed 1-12-21	100%
7	Milestone receiving material	291 days	Fri 18-2-22	Fri 31-3-23	93%
8	Construction material	1 day	Tue 15-3-22	Tue 15-3-22	100%
9	Anchor bolts	1 day	Fri 25-3-22	Fri 25-3-22	100%
10	Piping material	1 day	Mon 4-4-22	Mon 4-4-22	100%
11	V-belt guards	1 day	Wed 6-4-22	Wed 6-4-22	100%
12	Inter/After coolers	1 day	Mon 27-6-22	Mon 27-6-22	100%
13	Pulsation damper in/out-let	1 day	Thu 30-6-22	Thu 30-6-22	100%
14	Compressor 12kW	1 day	Fri 18-2-22	Fri 18-2-22	100%
15	Compressor 35 kW	1 day	Fri 18-2-22	Fri 18-2-22	100%
16	Y-strainers	1 day	Wed 20-4-22	Wed 20-4-22	100%
17	Electrical items	1 day	Fri 9-9-22	Fri 9-9-22	75%
18	Gauges	1 day	Wed 24-8-22	Wed 24-8-22	100%
19	Motor 45 kW Nitrogen	1 day	Wed 6-4-22	Wed 6-4-22	100%
20	Motor 15 Kw air	1 day	Wed 6-4-22	Wed 6-4-22	100%
21	Transmitters	1 day	Fri 22-7-22	Fri 22-7-22	100%
22	Grating	1 day	Fri 20-5-22	Fri 20-5-22	100%
23	Valves	1 day	Mon 23-5-22	Mon 23-5-22	100%
24	Junction boxen	1 day	Tue 25-10-22	Tue 25-10-22	100%
25	PLC	1 day	Fri 31-3-23	Fri 31-3-23	0%
26	Compressor B - Air booster	265 days	Mon 28-3-22	Fri 31-3-23	100%
27	Construction	30 days	Mon 28-3-22	Fri 6-5-22	100%
33	Prefab piping	80 days	Tue 12-4-22	Mon 1-8-22	100%
42	Painting Construction	6 days	Mon 23-5-22	Mon 30-5-22	100%
45	Components	33 days	Wed 1-6-22	Fri 15-7-22	100%
49	Painting pipes & components	10 days	Tue 2-8-22	Mon 15-8-22	100%
52	Skid Piping	11 days	Wed 17-8-22	Wed 31-8-22	100%
55	Tubing & Instrumentation	8 days	Fri 10-2-23	Tue 21-2-23	100%
58	Electric	60 days	Mon 9-1-23	Fri 31-3-23	100%
62	Compressor A - Nitrogen Gas Booster	260 days	Mon 4-4-22	Fri 31-3-23	100%
63	Construction	25 days	Mon 4-4-22	Fri 6-5-22	100%
69	Prefab piping	57 days	Fri 6-5-22	Mon 25-7-22	100%
77	Painting Construction	6 days	Tue 10-5-22	Tue 17-5-22	100%
80	Components	29 days	Wed 1-6-22	Mon 11-7-22	100%
84	Painting pipes & components	6 days	Mon 1-8-22	Mon 8-8-22	100%
87	Skid Piping	11 days	Mon 8-8-22	Mon 22-8-22	100%
90	Tubing & Instrumentation	92 days	Mon 17-10-22	Tue 21-2-23	100%
93	Electric	163 days	Wed 17-8-22	Fri 31-3-23	100%
97	Finalising	25 days	Thu 23-3-23	Wed 26-4-23	25%
98	Personal protection	8 days	Wed 5-4-23	Fri 14-4-23	25%
100	Documents	1 day	Mon 17-4-23	Mon 17-4-23	0%
103	Inspection	22 days	Thu 23-3-23	Fri 21-4-23	67%
106	Packing & Shipping	3 days	Mon 24-4-23	Wed 26-4-23	0%

Package is ready for shipment.
