



Toase-eh Park Sanati Gohar Ofogh
Petrochemical Co.
**CONCEPTUAL, BASIC and DETAIL DESIGN
ENGINEERING OF STYRENE PARK OFFSITE**



ARKAN SANAT PAYDAR
Procurement & Construction

Document Title:
Time Schedule for Ru0001A / B-D-02

Document No.: EI027-ASP-VD-ME-SCH-015

Rev. R0

Page 1 of 6

STYRENE PARK OFFSITE

Time Schedule for Ru0001A / B-D-02

Rev.	Issued Date	DESCRIPTION	PREPARED	CHECKED	APPROVED
R0	15-Apr-25	IFA	F.Malekifar	M.Yasini	S.Derakhshande



Toase-che Park Sanati Gohar Ofogh
Petrochemical Co.
**CONCEPTUAL, BASIC and DETAIL DESIGN
ENGINEERING OF STYRENE PARK OFFSITE**



ARKAN SANAT PAYDAR
Procurement & Construction

Document Title:
Time Schedule for Ru0001A / B-D-02

Document No.: EI027-ASP-VD-ME-SCH-015


Rev. R0

Page 2 of 6

REVISION RECORD SHEET

Page Page	Revisions							Page	Revisions						
	R0	R1	R2	R3	R4	R5	R6		R0	R1	R2	R3	R4	R5	R6
1	X							41							
2	X							42							
3	X							43							
4	X							44							
5	X							45							
6	X							46							
7								47							
8								48							
9								49							
10								50							
11								51							
12								52							
13								53							
14								54							
15								55							
16								56							
17								57							
18								58							
19								59							
20								60							
21								61							
22								62							
23								63							
24								64							
25								65							
26								66							
27								67							
28								68							
29								69							
30								70							
31								71							
32								72							
33								73							
34								74							
35								75							
36								76							
37								77							
38								78							
39								79							
40								80							


ID	WBS	Task Name	Duration	شروع	پایان	W.V	Qtr 1, 2025			Qtr 2, 2025		
							Jan	Feb	Mar	Apr	May	Jun
0		HAMIYAN SANAT	81 days	1403/12/2	1404/3/4	100						
1	A	Engineering & Designing	67 days	1403/12/2	1404/2/18	5						
2	A.2	Vessels 1&2	67 days	1403/12/2	1404/2/18	5						
3	A.2.1	Engineering & Designing	67 days	1403/12/2	1404/2/18	5						
4	B	PROCUREMENT	4 days	1403/12/14	1403/12/18	30						
5	B.6	Vessels 1&2	4 days	1403/12/14	1403/12/18	30						
6	B.6.1	Mechanical	4 days	1403/12/14	1403/12/18	12						
7	B.6.1.4	Purchase order	1 day	1403/12/14	1403/12/14	3						
8	B.6.1.5	Inspection	2 days	1403/12/15	1403/12/16	6						
9	B.6.1.6	Delivery at site	1 day	1403/12/18	1403/12/18	3						
10	B.6.2	Paint Material	4 days	1403/12/14	1403/12/18	18						
11	B.6.2.4	Purchase order	1 day	1403/12/14	1403/12/14	4.5						
12	B.6.2.5	Inspection	2 days	1403/12/15	1403/12/16	9						
13	B.6.2.6	Delivery at site	1 day	1403/12/18	1403/12/18	4.5						
14	C	CONSTRUCTION	52 days	1403/12/19	1404/2/17	42						
15	C.3	Vessels 1&2	52 days	1403/12/19	1404/2/17	42						
16	C.3.1	Mechanical	45 days	1403/12/19	1404/2/9	27						
17	C.3.1.9	Elliptical Head	19 days	1403/12/19	1404/1/10	9.33						
18	C.3.1.9.2	Elliptical Head 1 & 2	19 days	1403/12/19	1404/1/10	9.33						
19	C.3.1.9.2.6	Cutting	3 days	1403/12/19	1403/12/21	1.47						
20	C.3.1.9.2.7	Grinding	2 days	1403/12/22	1403/12/23	0.98						
21	C.3.1.9.2.8	Beveling	2 days	1403/12/25	1403/12/26	0.98						

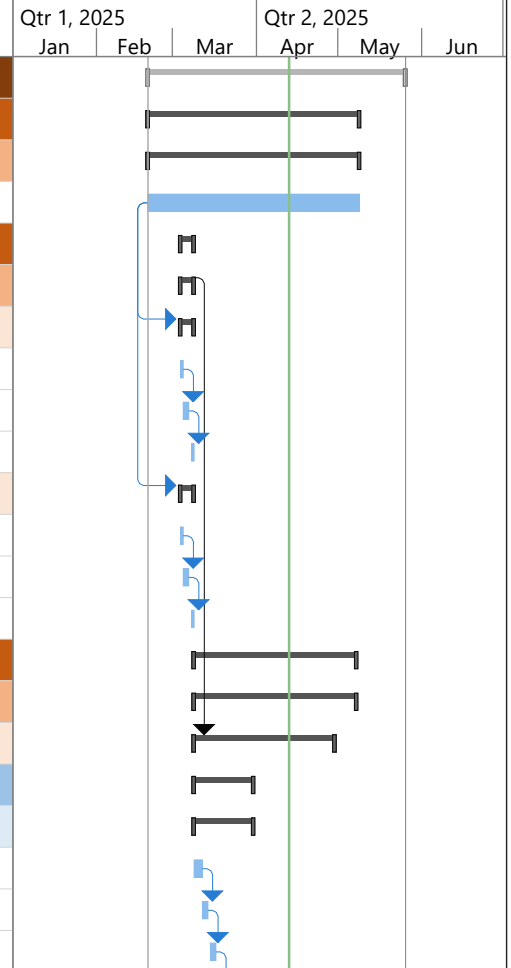

Project: HAMIYAN SANAT
Date: 4/13/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID	WBS	Task Name	Duration	شروع	پایان	W.V	Qtr 1, 2025			Qtr 2, 2025		
							Jan	Feb	Mar	Apr	May	Jun
22	C.3.1.9.2.9	Fitup	2 days	1403/12/27	1403/12/28	0.98						
23	C.3.1.9.2.10	Head manufacturing	10 days	1403/12/29	1404/1/10	4.92						
24	C.3.1.10	Shell	8 days	1404/1/11	1404/1/19	7.85						
25	C.3.1.10.8	Shell Plate Course1	8 days	1404/1/11	1404/1/19	3.93						
26	C.3.1.10.8.0	Cutting	1 day	1404/1/11	1404/1/11	0.49						
27	C.3.1.10.8.1	Grinding	1 day	1404/1/12	1404/1/12	0.49						
28	C.3.1.10.8.2	Beveling	1 day	1404/1/13	1404/1/13	0.49						
29	C.3.1.10.8.3	Rolling	3 days	1404/1/14	1404/1/17	1.48						
30	C.3.1.10.8.4	Welding	2 days	1404/1/18	1404/1/19	0.98						
31	C.3.1.10.9	Shell Plate Course2	8 days	1404/1/11	1404/1/19	3.92						
32	C.3.1.10.9.0	Cutting	1 day	1404/1/11	1404/1/11	0.49						
33	C.3.1.10.9.1	Grinding	1 day	1404/1/12	1404/1/12	0.49						
34	C.3.1.10.9.2	Beveling	1 day	1404/1/13	1404/1/13	0.49						
35	C.3.1.10.9.3	Rolling	3 days	1404/1/14	1404/1/17	1.47						
36	C.3.1.10.9.4	Welding	2 days	1404/1/18	1404/1/19	0.98						
37	C.3.1.16	Welding Shell to Shell & Shell to Head	9 days	1404/1/20	1404/1/30	4.42						
38	C.3.1.16.10	Fitup of Shell Course 1 to Shell Course 2	3 days	1404/1/20	1404/1/23	1.47						
39	C.3.1.16.10.0	Fitup	1 day	1404/1/20	1404/1/20	0.49						
40	C.3.1.16.10.1	Welding	2 days	1404/1/21	1404/1/23	0.98						
41	C.3.1.16.11	Fitup of Shell Course 1 to Head 2	3 days	1404/1/24	1404/1/26	1.47						
42	C.3.1.16.11.0	Fitup	1 day	1404/1/24	1404/1/24	0.49						
43	C.3.1.16.11.1	Welding	2 days	1404/1/25	1404/1/26	0.98						

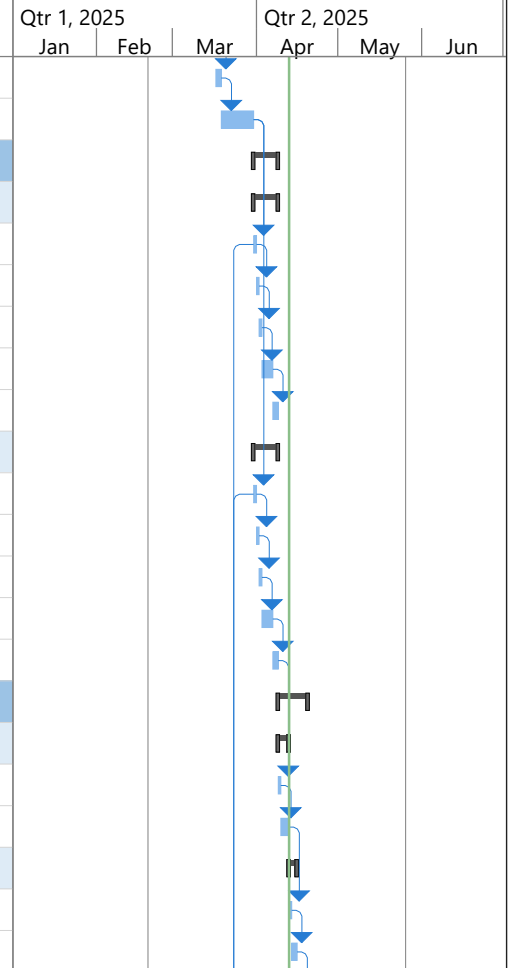

Project: HAMIYAN SANAT
Date: 4/13/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	WBS	Task Name	Duration	شروع	پایان	W.V	Qtr 1, 2025			Qtr 2, 2025		
							Jan	Feb	Mar	Apr	May	Jun
44	C.3.1.16.12	Fitup of Shell Course 2 to Head 2	3 days	1404/1/27	1404/1/30	1.48						
45	C.3.1.16.12	Fitup	1 day	1404/1/27	1404/1/27	0.49						
46	C.3.1.16.12	Welding	2 days	1404/1/28	1404/1/30	0.99						
47	C.3.1.14	Saddle	19 days	1404/1/11	1404/2/1	1.96						
48	C.3.1.14.4	Cutting	1 day	1404/1/11	1404/1/11	0.49						
49	C.3.1.14.5	Fitup	1 day	1404/1/12	1404/1/12	0.49						
50	C.3.1.14.6	Welding	2 days	1404/1/31	1404/2/1	0.98						
51	C.3.1.15	Nozzle	7 days	1404/2/2	1404/2/9	3.44						
52	C.3.1.15.6	Cutting	1 day	1404/2/2	1404/2/2	0.49						
53	C.3.1.15.7	Beveling	1 day	1404/2/3	1404/2/3	0.49						
54	C.3.1.15.8	Fitup	2 days	1404/2/4	1404/2/6	0.98						
55	C.3.1.15.9	Welding	3 days	1404/2/7	1404/2/9	1.48						
56	C.3.2	Painting	4 days	1404/2/14	1404/2/17	15						
57	C.3.2.2	External Painting	4 days	1404/2/14	1404/2/17	15						
58	C.3.2.2.3	Blasting	1 day	1404/2/14	1404/2/14	3.75						
59	C.3.2.2.4	Painting	3 days	1404/2/15	1404/2/17	11.25						
60	D	PRE COMMISSIONING & COMMISSIONING	8 days	1404/2/10	1404/2/18	18						
61	D.3	Vessels 1&2	8 days	1404/2/10	1404/2/18	18						
62	D.3.1	Pre Commissioning	3 days	1404/2/10	1404/2/13	12						
63	D.3.1.3	Hydrostatic test	1 day	1404/2/10	1404/2/10	4						
64	D.3.1.4	N2 Filling Procedure	2 days	1404/2/11	1404/2/13	8						
65	D.3.2	COMMISSIONING	1 day	1404/2/18	1404/2/18	6						

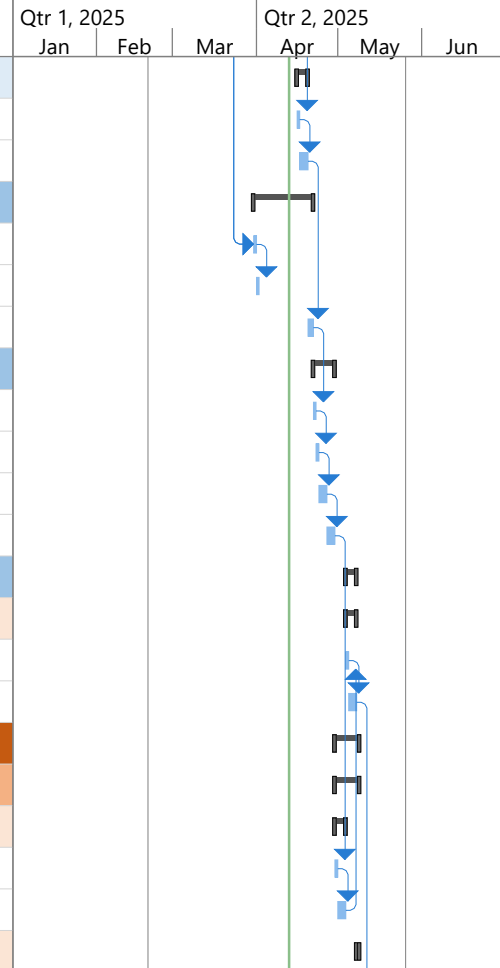

Project: HAMIYAN SANAT
Date: 4/13/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	WBS	Task Name	Duration	شروع	پایان	W.V	Qtr 1, 2025			Qtr 2, 2025		
							Jan	Feb	Mar	Apr	May	Jun
66	D.3.2.2	Tank Delivery to client	1 day	1404/2/18	1404/2/18	6						
67	E	FINAL BOOK	14 days	1404/2/20	1404/3/4	5						
68	E.2	Vessels 1&2	14 days	1404/2/20	1404/3/4	5						
69	E.2.1	Final Book	14 days	1404/2/20	1404/3/4	5						

Project: HAMIYAN SANAT
Date: 4/13/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
