



Toase-eh Park Sanati Gohar Ofogh Petrochemical Co.

**CONCEPTUAL, BASIC and DETAIL DESIGN
ENGINEERING OF STYRENE PARK OFFSITE**

Document Title: Project Time Schedule for Cartridge Filter

Document No. : EI027-ENR-VD-GE-SCH-003



Rev.: R1

Page 1 of 5

STYRENE PARK OFFSITE

Document Title:

**Project Time Schedule
for
Cartridge Filter**

Rev.	Issued Date	DESCRIPTION	PREPARED	CHECKED	APPROVED
R1	3/10/2024	Issued for Approve	M.Akbarpour	A.Ajami	H.Keshmiri
R0	2/21/2024	Issued for Approve	M.Akbarpour	A.Ajami	H.Keshmiri



Toase-eh Park Sanati Gohar Ofogh Petrochemical Co.
**CONCEPTUAL, BASIC and DETAIL DESIGN ENGINEERING OF STYRENE PARK
 OFFSITE**



Document Title: Project Time Schedule for Cartridge Filter

Document No. : EI027-ENR-VD-GE-SCH-003

Rev.: R1

Page 2 of 5

Page	Revisions							Page	Revisions						
	R0	R1	R2	R3	R4	R5	R6		R0	R1	R2	R3	R4	R5	R6
1	X	X						41							
2	X	X						42							
3	X	X						43							
4	X	X						44							
5	X	X						45							
6								46							
7								47							
8								48							
9								49							
10								50							
11								51							
12								52							
13								53							
14								54							
15								55							
16								56							
17								57							
18								58							
19								59							
20								60							
21								61							
22								62							
23								63							
24								64							
25								65							
26								66							
27								67							
28								68							
29								69							
30								70							
31								71							
32								72							
33								73							
34								74							
35								75							
36								76							
37								77							
38								78							
39								79							
40								80							



Cartridge Filter



Activity ID	Activity Name	W.F	Planned Duration	Start	Finish	2024											
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
Cartridge Filter						100.00											
Milestone						240d											
A1000	Start	0.00	0d	02/10/2024													
A1010	Advance Payment	0.00	0d	02/10/2024													
A1020	Finish	0.00	0d		10/06/2024												
Engineering						10.00											
General						0.80											
A1030	Vendor Print Index and Schedule (VPIS) for Cartridge Filter	0.20	15d	02/10/2024	02/24/2024	Vendor Print Index and Schedule (VPIS) for Cartridge Filter											
A1050	Project Time Schedule for Cartridge Filter	0.16	12d	02/27/2024	03/09/2024	Project Time Schedule for Cartridge Filter											
A1040	Sub Vendor List for Cartridge Filter	0.16	12d	03/16/2024	03/27/2024	Sub Vendor List for Cartridge Filter											
A1060	Commissioning Spare Part List for Cartridge Filter	0.08	14d	06/04/2024	06/17/2024	Commissioning Spare Part List for Cartridge Filter											
A1070	Two Years Operation Spare Parts List for Cartridge Filter	0.08	14d	06/04/2024	06/17/2024	Two Years Operation Spare Parts List for Cartridge Filter											
A1080	Final Book Index for Cartridge Filter	0.04	14d	08/07/2024	08/20/2024	Final Book Index for Cartridge Filter											
A1090	Final Book for Cartridge Filter	0.08	30d	08/21/2024	09/19/2024	Final Book for Cartridge Filter											
Quality Control						0.50											
A1100	Inspection And Test Plan for Cartridge Filter	0.18	14d	03/16/2024	03/29/2024	Inspection And Test Plan for Cartridge Filter											
A1120	Preservation , Packaging, And Shipping Procedure for Cartridge Filter	0.10	14d	03/30/2024	04/12/2024	Preservation , Packaging, And Shipping Procedure for Cartridge Filter											
A1110	Welding Procedure Specification & Qualification Records for Cartridge Filter	0.10	14d	04/25/2024	05/08/2024	Welding Procedure Specification & Qualification Records for Cartridge Filter											
A1130	Test Procedures for Cartridge Filter	0.13	14d	04/25/2024	05/08/2024	Test Procedures for Cartridge Filter											
Process						2.00											
A1150	PFD for Cartridge Filter	0.70	15d	02/15/2024	02/29/2024	PFD for Cartridge Filter											
A1160	P&ID for Cartridge Filter	0.70	15d	03/01/2024	03/15/2024	P&ID for Cartridge Filter											
A1170	Process Description for Cartridge Filter	0.40	15d	03/16/2024	03/30/2024	Process Description for Cartridge Filter											
A1140	Installation, Operating and Maintenance Manual for Cartridge Filter	0.20	10d	07/28/2024	08/06/2024	Installation, Operating and Maintenance Manual for Cartridge Filter											
Mechanical						2.50											
A1190	Equipment Data Sheet-Cartridge Filter	0.62	13d	03/16/2024	03/28/2024	Equipment Data Sheet-Cartridge Filter											
A1210	Strength Calculation-Cartridge Filter	0.62	13d	03/29/2024	04/10/2024	Strength Calculation-Cartridge Filter											
A1230	General Arrangement Drawing-Cartridge Filter	0.76	14d	04/11/2024	04/24/2024	General Arrangement Drawing-Cartridge Filter											
A1240	Name Plate Drawing for Cartridge Filter	0.13	10d	04/25/2024	05/04/2024	Name Plate Drawing for Cartridge Filter											
A1250	Ladder & Platform Drawing for Cartridge Filter	0.38	14d	04/25/2024	05/08/2024	Ladder & Platform Drawing for Cartridge Filter											
Piping						2.00											
A1260	GAD For Package for Cartridge Filter	1.30	20d	05/09/2024	05/28/2024	GAD For Package for Cartridge Filter											
A1270	MTO for Piping for Cartridge Filter	0.70	20d	05/29/2024	06/17/2024	MTO for Piping for Cartridge Filter											
Instrument						1.50											
A1280	Instrument List for Cartridge Filter	0.30	15d	03/16/2024	03/30/2024	Instrument List for Cartridge Filter											
A1300	Junction Boxes Wiring Diagrams And Outline Drawing for Cartridge Filter	0.38	15d	03/31/2024	04/14/2024	Junction Boxes Wiring Diagrams And Outline Drawing for Cartridge Filter											

█ Actual Level of Effort █ Critical Remaining Work
█ Primary Baseline ◆ Milestone
█ Actual Work ▬ summary
█ Remaining Work

Contractor's Signature


Owner's Signature



Cartridge Filter



Activity ID	Activity Name	W.F	Planned Duration	Start	Finish	2024																	
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct								
A1330	Junction Boxes Wiring Diagrams And Outline Drawing	0.23	15d	04/06/2024	04/20/2024																		
A1290	I/O List for Cartridge Filter	0.15	15d	04/07/2024	04/21/2024																		
A1320	Instrument Cable List for Cartridge Filter	0.23	15d	04/14/2024	04/28/2024																		
A1310	Hook Up Drawing for Cartridge Filter	0.23	20d	05/13/2024	06/01/2024																		
Civil		0.70	20d	05/29/2024	06/17/2024																		
A1340	Foundation Plans With Static/Dynamic Loads, And Bolts Detail for Cartridge Filter	0.70	20d	05/29/2024	06/17/2024																		
Procurement		50.00	119d	04/15/2024	08/11/2024																		
Plate		13.50	25d	04/25/2024	05/19/2024																		
A1350	Inquiry	1.35	7d	04/25/2024	05/01/2024																		
A1360	P.O (Purchase Order)	5.40	6d	05/02/2024	05/07/2024																		
A1370	Inspection & Packing	5.40	9d	05/08/2024	05/16/2024																		
A1380	Delivery to Shop	1.35	3d	05/17/2024	05/19/2024																		
Nozzle		6.76	32d	04/25/2024	05/26/2024																		
A1410	Inquiry	0.68	8d	04/25/2024	05/02/2024																		
A1420	P.O (Purchase Order)	2.70	5d	05/03/2024	05/07/2024																		
A1440	Inspection & Packing	2.70	14d	05/08/2024	05/21/2024																		
A1450	Delivery to Shop	0.68	5d	05/22/2024	05/26/2024																		
Instrument		9.48	50d	04/15/2024	06/03/2024																		
A1460	Inquiry	0.95	15d	04/15/2024	04/29/2024																		
A1470	P.O (Purchase Order)	0.95	5d	04/30/2024	05/04/2024																		
A1480	Manufacturing	5.68	20d	05/05/2024	05/24/2024																		
A1490	Inspection & Packing	0.95	5d	05/25/2024	05/29/2024																		
A1500	Delivery to Shop	0.95	5d	05/30/2024	06/03/2024																		
Material for Skid		6.76	25d	05/29/2024	06/22/2024																		
A1750	Inquiry	0.68	7d	05/29/2024	06/04/2024																		
A1760	P.O (Purchase Order)	2.70	6d	06/05/2024	06/10/2024																		
A1770	Inspection & Packing	2.70	9d	06/11/2024	06/19/2024																		
A1780	Delivery to Shop	0.68	3d	06/20/2024	06/22/2024																		
Pipe, Fitting & Valve		13.50	55d	06/18/2024	08/11/2024																		
A1510	Inquiry	1.35	30d	06/18/2024	07/17/2024																		
A1520	P.O (Purchase Order)	5.40	10d	07/18/2024	07/27/2024																		
A1530	Inspection & Packing	5.40	10d	07/28/2024	08/06/2024																		
A1540	Delivery to Shop	1.35	5d	08/07/2024	08/11/2024																		
Fabrication		30.00	120d	05/20/2024	09/16/2024																		
Cartridge Filter		30.00	120d	05/20/2024	09/16/2024																		
Pressure Vessel & Ladder Platform		19.50	120d	05/20/2024	09/16/2024																		

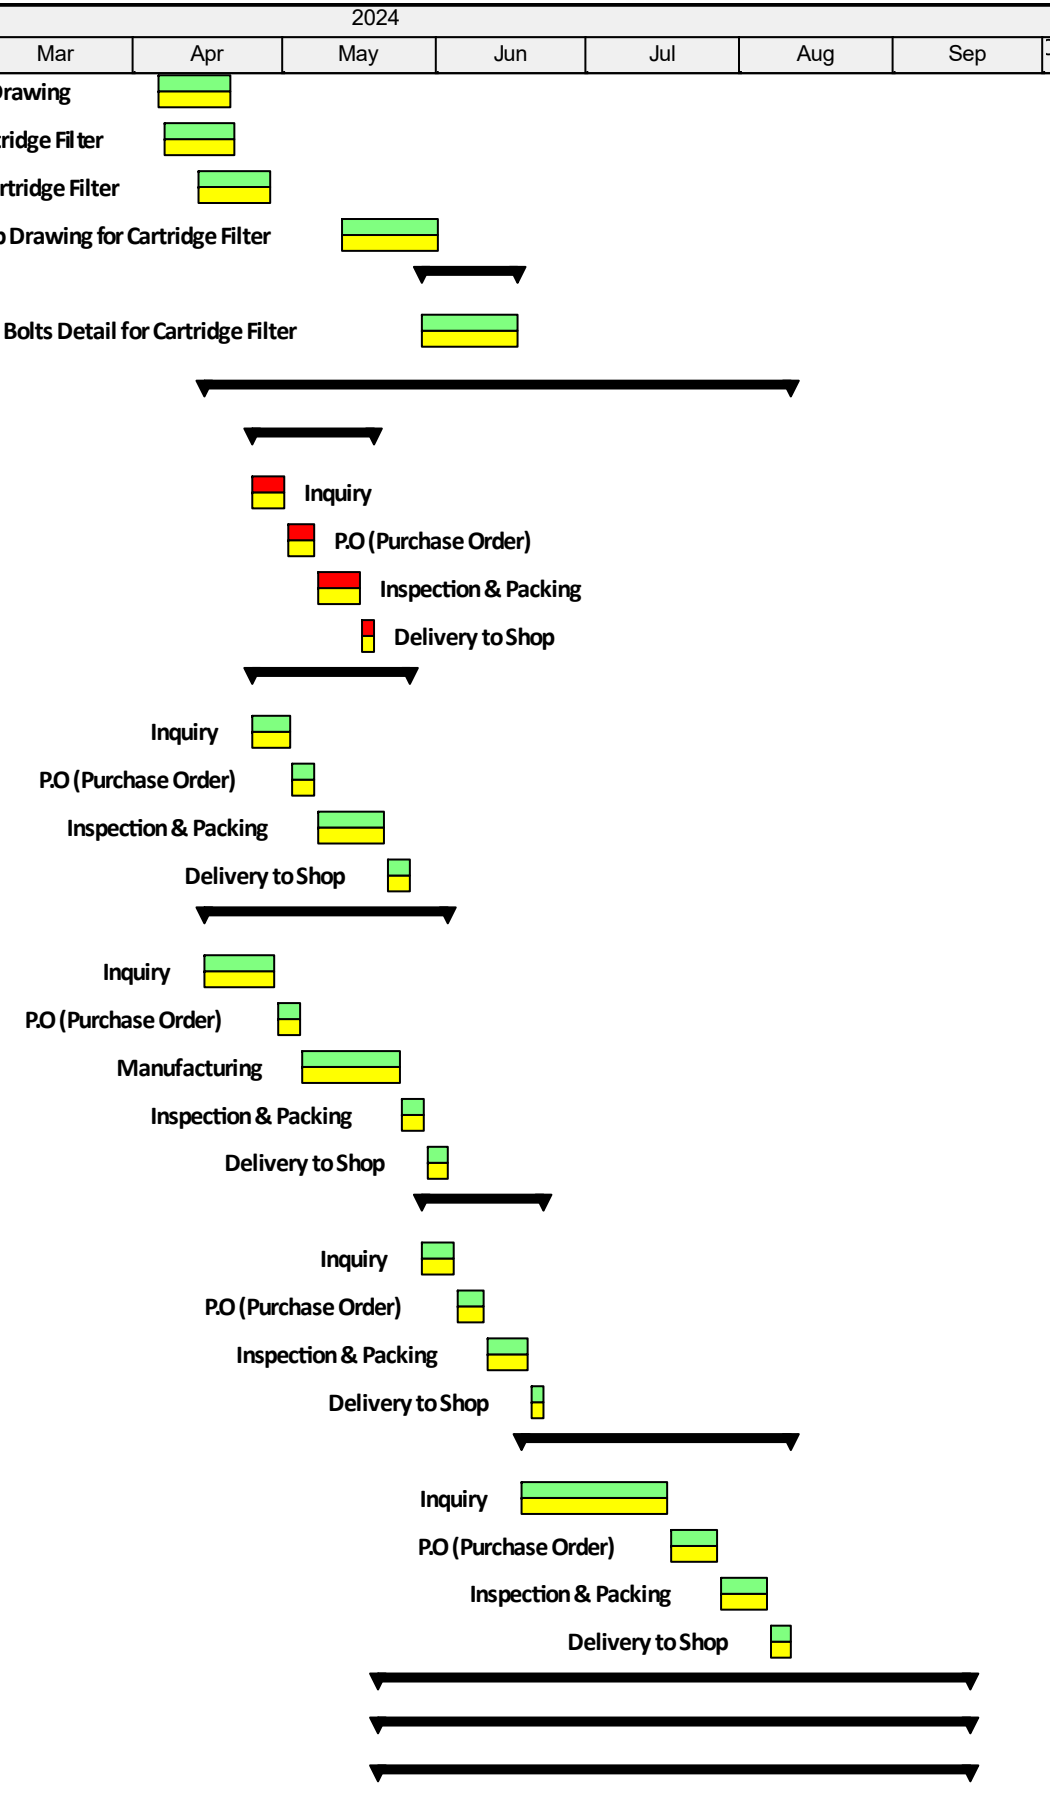

■ Actual Level of Effort ■ Critical Remaining Work
■ Primary Baseline ◆ Milestone
▬ Actual Work ▬ summary
▬ Remaining Work

Contractor's Signature

Owner's Signature

